Getting Started with ConceptDraw PROJECT 15 for Windows

CS Odessa corp.

Contents

GETTING STARTED WITH CONCEPTDRAW PROJECT	3
CREATING PROJECTS	4
ASSIGNING RESOURCES	5
SETTING THE CALENDAR	7
ADDING DETAILS MILESTONE HYPERNOTE	8
MANAGING MULTIPLE PROJECTS	9
PROJECT REPORTS	10
PRESENTING YOUR PROJECT	11
INTEGRATING WITH OTHER CONCEPTDRAW OFFICE APPLICATIONS CONCEPTDRAW DIAGRAM CONCEPTDRAW MINDMAP	12
WORKING WITH OTHER APPLICATIONS	14
SOLUTIONS	14
VIDEO ROOM	14
SAMPLES	14
NO-CHARGE SUPPORT	14
CROSS-PLATFORM LICENSING	15
MULTI-DISPLAY SUPPORT	15
WINDOWS 64-BIT SUPPORT	15
ABOUT CS ODESSA	15
FREQUENTLY ASKED QUESTIONS	16
TABLE OF FIGURES SUPPORT	17
KEYBOARD SHORTCUTS	18

GETTING STARTED WITH CONCEPTDRAW PROJECT

Thank you for your interest in ConceptDraw® PROJECT 15! To begin with, let's install the program on your system. To install the product, and activate your trial license:

- 1. Navigate your web browser to www.conceptdraw.com and click Sign In.
- 2. Fill in the form with your information, and then click Submit.
- Check your email for the message from support@ConceptDraw.com that contains your confirmation link. (Spam filters may catch this message. If you don't see the email within a few minutes, check your "Junk" or "Spam" folders.)
- 4. Follow the link to confirm your account, and then click **Download product**.
- 5. Once the download is complete, run the installation file.
- 6. Follow all the on-screen instructions to complete the installation.
- Once the installation is completed, ConceptDraw STORE runs automatically. The trial licenses listed in your account will be delivered to your computer automatically through your internet connection.
- 8. Congratulations! Your FREE 21-day trial of ConceptDraw PROJECT has begun.

CREATING PROJECTS

The default view for a new project is the Gantt Chart.

The left pane of this chart displays a list of Tasks. The right pane displays a calendar and timeline of those tasks.

To begin managing a new project, you will need to define the individual Tasks that must

be completed to deliver it. Click the Add button \blacksquare on the Home toolbar to create a new Task.




Figure 1: Gantt Chart

Then name the Task, and assign its duration. You can do so by double-clicking on the fields in the left pane of the Gantt chart, and then typing on your keyboard.

Tasks are usually grouped into larger Phases. Use the Indent button **Sec** on the Home toolbar to subordinate a Task, thereby making the dominant item into a Phase. You cannot edit a Phase's duration. The duration of a Phase is determined by the duration of all the Tasks within it.

Often, one Task must be completed before another can begin. To establish a relationship between Tasks, select two or more Tasks on the Gantt chart, and then click the Link

button **F** on the Home toolbar. Editing the duration of linked Tasks will automatically adjust their position on the Gantt chart.

ASSIGNING RESOURCES

Once you have outlined the Tasks that comprise your project, the next step is to assign Resources to those Tasks.

Select a Task on the Gantt chart, and then open the Assign Resources panel in the Panels list on the View tab. Click the check box next to a Resource to assign it to the selected Task.

August 2023			S	eptember	2023			October	2023		As	sign Resources		ųх
31 w32	w33	w34	w35	w36	w37	w38	w39	w40	w41	W	E	Resource	Units	Work ^
•	8/7/2023											Bob's Excavation	100.00 %	
			-			-							100.00 %	120 11
	→ •	8/14/202	23									Surveyor		
		l	+		Surv	vevor 1						Surveyor 1		
				_		1						Surveyor 2		
				1		•	Bot	o's Exca	vation; E	xca		Baker Flooring		
					•						1		1.00	
			_									Truck		
					Bob's Ex	cavatio	n [100 9	6]; Exca	vator [1	1		Concrete mixer		
				-								Tom Sheldon		
									-			Rich Gannon		
						ſ			Surv	eyor		Joe Smith		
						4	□ ₽ Bak	er Floor	ing; Con	crete		Tom Farrel		
					_		<u> </u>					Mike Grabowski		
						•	 Bot 	o's Exca	vation; C	onci		Jane Postal		
						Survey	or 2					Pat O'Tormey		
					-			D-I				HVAC R US		
					-			Dar	er Floor	ing,		Exteriors Unlimited		
												Exteriors entitled		>
										>				
										- /				

Figure 2: Assign Resources panel

There are five kinds of Resources: Work,; Material; Cost; Equipment and Company. Work resources are those with a cost over time. Other resource types have a fixed cost per unit.

	Resource	Units	Work		
	Excavation			<u>۵۵</u>	
/	Bob's Excavation	50.00 %	64 h	4	
1	Excavator	1.00	-	<u>مه</u>	
	Truck			<u>ه</u>	
	Bob's Excavation			4	
V	Excavator	1.00		≤	
	Truck				Work
	Surveyor				Material
	Surveyor 1				
	Surveyor 2			\$	Cost
V	Surveyor 2	50.00 %	64 h	6	Equipment
	Surveyor 1				Company
	Flooring			-	
	Baker Flooring			4	
	Concrete mixer			<u>ه</u>	
	Baker Flooring			4	
1	Concrete mixer	1.00	-	<u>ه</u>	

Figure 3: List of Resource Types

For detailed information on your project's Resources, click the Resources button on the Home toolbar to view the Resource Sheet

le -	Home View Share												Sec	arch.	n e
	Cut Arial ~ 11 - Copy = Wrap Text Ab A A rormat Text			Hultiproject	Microrep	orts Add Ir	Add Subitem	Link Unitek	Indent Move	2 10	Markes 19	Calendar Calendar	Save Baseline	Find Re	place Smar diting
	Name	Туре	Cost	Group		E-4	fail .	Notes							
1 1	Bob's Excavation	Work	200 \$/h		b	ob excavation	@gmail.com		₩.						
2 *	Surveyor 1	Work	100 S/h	Surveyor	s	urveyor2@gm	ail.com		7						
3 *	Baker Flooring	Work	160 S/h		b	aker flooring(2gmail.com		-						
4 4	Surveyor 2	Work	100 S/h	Surveyor	2	urveyor2@arr	ail.com								
6 🐓	Excavator	Equipment	700 \$												
s 🐓	Truck	Equipment	700 \$												
7 🍫	Concrete mixer	Equipment	700 \$												
8 🌮	Tom Sheldon	Work	150 S/h												
9 🍫	Rich Gannon	Work	150 S/h												
10 *	Joe Smith	Work	150 S/h						*						
1 5	Tom Farrell	Work	150 S/h												
2 *	Mike Grabowski	Work	150 \$/h						*						
13 *	Jane Postal	Work	150 S/h						× .						
4 5	Pat O'Tormey	Work	150 \$/h												
15 *	HVAC R Us	Work	150 S/h						*						
Preview															

Figure 4: Resource Sheet

Once you have detailed and assigned your Resources, the Resource Usage View will tell you at a glance if your Work Resources (i.e., employees) are over taxed.

This dashboard displays the amount of work assigned each day to each Work Resource. Overworked Resources appear as red bars on the timeline.

Click the + next to each Resource to view the Tasks it is assigned to.

📓 🔲 🗖 💾 🖱 🖳 📕 📕			[Comme	ercial Con	struction n	nultiproject n	ew.cdpz ·	Resource	Usage View]	Concept	Draw PR	OJECT							-	ц)
File Home View Share																				ñ (
Gontt Chart Chart Chart			le Expand C All	;	E Expand Collapse Outline I		n filter Iow Phase		▼S × g w/Highlight	• •		Iheme	; 1	• • •	Assig	al Path aned Resource v Text Roxes Show/Hide	Boscline			Windows
Name	Project Name	Expens 20 Aug 21		26 2	36,27 Aug : 7 28 2		01 02	W38, 03	sep 2023	07 08	WG	sr, to Sep 2 0 11 12		15 16		/ Sep 2023	21 22	w3	8, 24 Sep 21	27 28
Bob's Excavation		148,8 100%	2005			21011			200	O14		COOK I	1000			ECO15	MOONE		10	
Clearing and Site Grading	Construction	24,000							100%				100%			100%	_			
Excavation	Construction	25,600	100%			100%		10												
Concrete Piles	Construction	16,000											100%			1005				
Brick	Construction	40,000	100%			100%			100%				100%			100%	_		100%	
Venting	Construction	8,000 :							1	0%		100%								
Design provides Construction	Site Arrangement	17,600											100%			100%			10	
Design provides Construction	Lease a New Facility	17,600							1	0%			100%			100%				
Surveyor 1		19,20				100%			100%							100%				100%
Stake lines and grades	Construction	8,000 :				100%			100%											
Footings	Construction	11,200														100%				100%
Baker Flooring		84,48						1	0%	0%			500%				300%		200%	100%
Spread Footings	Construction	19,200							100%			-	100%			100%				
Walla	Construction	19,200											100%			100%				100%
	Construction	19,200							1	0%			100%			100%			100%	
Telephone, Security, and Flectrical	Construction	12,800							1	0%			100%			100%				
Design provides Construction	Lease a New Facility	14,080							1	0%			100%			100%				
		> <																		,
lide Preview																				
eady																I 4 🖡		V-d		++

Figure 5: Resource Usage View

SETTING THE CALENDAR

By default, ConceptDraw PROJECT assumes working hours are between 8am and 5pm, Monday through Friday. However, creating exceptions to this policy is easy.

Click Calendar button on the Home toolbar. This will open the Document Properties window.

From the Calendar tab of this window, you can designate non-default working hours for specific days, as well as non-working days.

You can also select a specific Work Resource from the drop down menu above the calendar to change working hours and days for that resource only.

eneral	Cal	endar	Adv	anced	ł					
Setting	n for	colony	dare							
Bob's			101.					✓ Reset	t to default 🛛 💌	
44 4		9	9-2023	3		Þ ÞÞ		ay working t		
Su	Мо	Tu	We	Th	Fr	Sa	L	Nonworkin	g	
27	28	29	30	31	1	2		From	То	
3	4	5	6	7	8	9		8:00 13:00	12:00 17:00	
10	11	12	13	14	15	16				
17	18	19	20	21	22	23				
24	25	26	27	28	29	30		£ ─		
1	2	3	4	5	6	7				
,										

Figure 6: Calendar

ADDING DETAILS

HYPERNOTE

To make referencing information outside the project file effortless, you can add Hyperlinks and text Notes to a Task, Phase, Resource or Project.

Select the item in question, and then select the Hypernote panel in the Panels list on the View tab.

The buttons at the bottom of the Hypernote pane allow you to quickly link to a website, a file or folder on your computer, an email address, or other object within your project file.

	pernote	д	1
Note			
	t of transaction focuses on the i make up an accoubt balance	individual transactions	
Нуре	rlinks		
Нуре Т	rlinks Link	Owner	
÷.		Owner Test of Transactions	
÷.	Link www.financial.com project.com	Test of Transactions Test of Transactions	
÷.	Link www.financial.com	Test of Transactions	
÷.	Link www.financial.com project.com	Test of Transactions Test of Transactions	
÷.	Link www.financial.com project.com	Test of Transactions Test of Transactions	
÷.	Link www.financial.com project.com	Test of Transactions Test of Transactions	

Figure 7: Hypernote panel

MILESTONE

You can set a Milestone in your Gantt chart by selecting a Task, and then clicking the "Milestone" checkbox in the Task pane. Milestones do not have duration, but they can be marked Completed by clicking the "Complete" checkbox.

Sep 2023	w37, 10 Sep 2023	w38, 17 S ^ Task 4	ι×
05 06 07 08 09	10 11 12 13 14 15 1	17 18	
Katherine	Smith	Info	
		Name: Cash and Equivalents	
		Duration: Minutes V	
	Katherine S	ith Complete:	
	Denise Morston		
		Milestone:	
	9/13/2023	Priority:	
	9/13/2023	Danica M Marker: No marker	
		Denise M Marker: No marker V	
	L+		
	-++ 9/13/2023		
	9/13/2023	Actual: 0 \$	
	9/13/2023	Dates	
		Start: 9/13/2023 8:00 AM	
		Finish: 9/13/2023 8:00 AM	
		Deadline: 3/ 1/2019 12:00 AM ~	
	-+- 9/13/2023	Scheduling	
	9/13/2023	Туре:	
		Effort driven:	
		Task types	
		Types: V	

Figure 8: Milestone on the Gantt chart

Getting Started with ConceptDraw PROJECT 15 for Windows

MANAGING MULTIPLE PROJECTS

ConceptDraw PROJECT allows you to manage multiple Projects in a single file.

Click Multiproject on the Home toolbar.

Multiproject view is similar to the Gantt chart, but the timeline is on a larger scale. Most of the controls on the toolbar work similarly to the Gantt chart, such as Add (to create new Projects) and Link (to create relationships between Projects).

However, you cannot edit the duration of a Project in Multiproject View. You must return to the Gantt chart and edit the timeline of the individual Project.

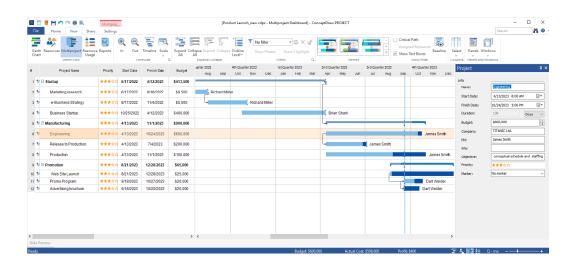


Figure 9: Multiproject View

Getting Started with ConceptDraw PROJECT 15 for Windows

PROJECT REPORTS

ConceptDraw PROJECT offers a variety of ways to report the status of your project.

These can be viewed by clicking the Solutions button on Home toolbar. This will open a side panel containing a vast array of choices for reporting on your project in spreadsheet (MS Excel®) format.

🔲 🗮 🗂 🗥 (* 🖷 🐘	[Commercial Construction_multiproject_new.cdpz - Reports View] - ConceptDraw PROJECT	
File Home View Share		A C
Gantt Resources Multiproject Resource Re Usage Select View	All All Level* Show Text	esources Baseline Select Panels Windows
olutions 4 ×	All Tasks Statuses	Report Parameters #
		▼Projects
Basic Projects	The "All Tasks Statuss" report created for your project represents the project's tasks that have to be executed in a period of time set by your according to your meeds. This report in a table from depicts the information on a volume of project work that is already completed, which tasks are now in progress, what volume of work on your project remains to be done for its completion and in what terms. All these conductions are based on the data accompanying the tasks in the project: the start and find hat dats, durations, the names of the corresponding responsible people, and the information about tasks completion stage in per cert.	Construction Construction Project Ste Arrangement Renewation Lease a New Facility
		▼Dates
		Report Period Document Timeline *
All Tasks Statuses	Unique (D) Numea Diversión Saint Envilo Campleire Recourse Nume	Start 7/28/2023
Air lasks statuses	1 New Product Launch 23.34 d File N.1897 NP.1.	
	Poss 1-Penning Bit (and) 23.14 (no.1374 arc.1374 dr.2374 dr.2374 dr.2374 25.14 25.14 25.14 25.14 25.14 25.14 25.14 25.14 25.14 25.14 25.14 25.14 25.1 25.14 25.1 25.	Finish 11/15/2023
i management in the	1 Dative the lawsh group 2.00 F institute, the source of the state of the source of th	▼Units
	² Define silve gash, 6.86 d. Feild, 189. Kall, 189. So (2010). https://doi.org/10.1016/j.jcond.feild/index.fe	
Milestones	1 Define launds gaad (aanst tinning and padalaty 0.020 J An IX 100 Hol X.100 100 N AN IX 100 N	Time Unit Use Current Documen
	1 Manuflygantour (if Acaded) 32.34.4 rents, Hex Work, Hex Work, Hex Stra	
	7 Meetilysband justness 32.24.4 mit 24.2024 Mar VIII 199 K. Mar VIII nr. Konstant	
	I Methywiaijadoes 04 20103 20103 20103 303 November (2)	
	2 Meetily-unline appendix-bias 0.00 # reals 200 meetiles 53.5% Meetiles for the second term for the sec	
Send Tasks List		
Image: state		
Only Installed Solutions		
adv	Budaet: 245.880 \$ Actual Cost: 230.400 \$ Profit: 15.480 \$ 🚍	

Figure 10: Project Report in Spreadsheet (MS Excel®) Format.

PRESENTING YOUR PROJECT

On the Share tab, you have three buttons for creating slides of specific views within your project.

Scroll to an area of the Gantt Chart or Resources Sheet, and use the Zoom controls on the View toolbar to focus on the area you wish to capture, and then click

Capture slide $\stackrel{f}{\Longrightarrow}$. Expand the Slide Preview tab at the bottom of the window by clicking on it and you will see the slides you have created thus far. You can save your slides as Portable Network Graphics files by clicking the PNG button $\stackrel{f}{\Longrightarrow}$.

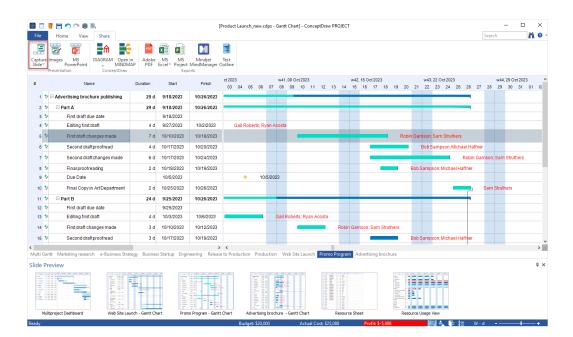


Figure 11: Project Slide Preview

INTEGRATING WITH OTHER CONCEPTDRAW OFFICE APPLICATIONS

Using all three programs in the ConceptDraw OFFICE suite in this way unlocks their true potential for increasing your productivity and facilitating your workflow.

CONCEPTDRAW DIAGRAM

If you have ConceptDraw DIAGRAM installed, the item Dashboards in the list of available reports on the Solutions panel can be used to generate drawings for tracking the status of your project at a glance.

Also, the DIAGRAM button and the Share tab can be used to draw a variety of diagrams, such as PERT charts and WBS (Work Breakdown Structure), suitable for printing and display.

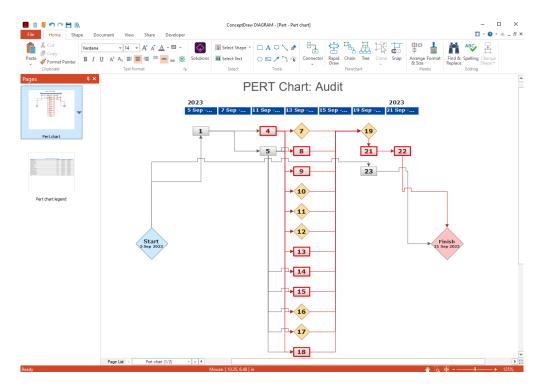


Figure 12: PERT Diagram

CONCEPTDRAW MINDMAP

If you also have ConceptDraw MINDMAP installed, you can instantly create a mind map

from your Gantt chart using the Open in MINDMAP button and the Share tab. This allows you to take full advantage of ConceptDraw MINDMAP's visual, non-linear organization capabilities for reorganizing your project, and add content via Brainstorming mode.

You can then send the mind map back to PROJECT to use its more detailed resource and task management capabilities.

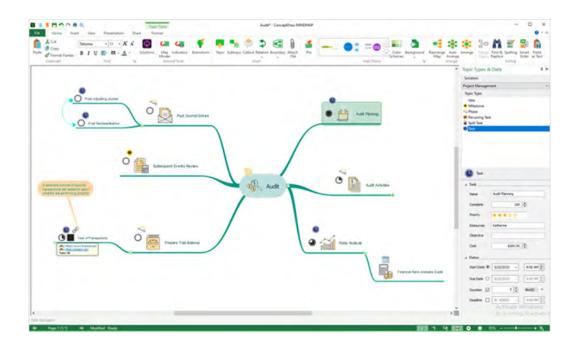


Figure 13: Project Mind Map

WORKING WITH OTHER APPLICATIONS

ConceptDraw PROJECT has the ability to export to a number of usable file formats, giving ConceptDraw users powerful flexibility in working with others. Expand the File tab to view all of ConceptDraw PROJECT's import and export options.

Exporting to MS Project® is one of the best ways to share your project. ConceptDraw PROJECT is thoroughly compatible with MS Project's, and can import from native .mpp format and export to MS Project XML files to make working across operating platforms not only possible, but effortless. ConceptDraw PROJECT is also import/export compatible with Mindjet® MindManager® files.

SOLUTIONS

ConceptDraw Solutions is an ever-growing collection of business-specific solutions and product add-ons that are available to add continued value after the initial purchase of a ConceptDraw product. For more information, visit www.conceptdraw.com/solution-park

SAMPLES

CS Odessa offers an online collection of professional samples designed to help Concept-Draw users achieve their best. ConceptDraw Samples shows many of the varieties of tasks and possibilities that the ConceptDraw Product Line can achieve. www.conceptdraw.com/samples/about-samples

NO-CHARGE SUPPORT

CS Odessa offers no-charge support for all licensed and trial users of ConceptDraw Products. ConceptDraw Maintenance Assurance P1 is also available to stay current with major updates to ConceptDraw Products. Getting Started with ConceptDraw PROJECT 15 for Windows

CROSS-PLATFORM LICENSING

CS Odessa is one of the only companies in the world that offers a cross-platform license. This means that if you want to install your product on a Mac and a PC for your use, you can do so with our license. Most companies require that you purchase a separate license for each platform.

MULTI-DISPLAY SUPPORT

ConceptDraw PROJECT supports working across multiple computer screens. You can open separate mind maps on different screens and copy-and-paste from one to the other.

WINDOWS 64-BIT SUPPORT

All ConceptDraw applications are compatible with Windows 10, 11 (64-bit certified).

ABOUT CS ODESSA

Founded in 1993, Computer Systems Odessa supplies cross-platform productivity tools and graphics technologies to professional and corporate users around the world.

From their headquarter in Odessa, Ukraine, CS Odessa sells internationally in over 150 countries, both directly and through resellers.

The ConceptDraw Productivity Line has won numerous awards, and is used by hundreds of thousands all over the world. For more information, visit www.conceptdraw.com

FREQUENTLY ASKED QUESTIONS

What is the difference between Technical Support and Maintenance Assurance P1?

Technical support is a no charge item provided to our customers and individuals trialing or products. Our Tech Support team is there to help you with installing, product activation, and product issues. Technical support is available by submitting a ticket via our web site, and by phone and email. Minor product upgrades are at no additional cost.

When purchased at the same time of you ConceptDraw Product purchase, Maintenance Assurance P1 provides you the next major release of your product at no additional cost. When the next major upgrade of the product becomes available you will be notified of its availability for download and installation.

Why is ConceptDraw STORE part of the product I purchased?

When you activate a purchased license for your product, that authorization is stored in the cloud, and then synchronized with your desktop product(s) using ConceptDraw STORE. We do this so if the unthinkable occurs and you have a catastrophic event with your computer such as a hard disk failure, you can log into your account on ConceptDraw.com and retrieve your license, saving you time and headaches.

The ConceptDraw STORE also manages the versioning of all of your products, and give you access to all of the additional business solutions found in the ConceptDraw Solution Park.

I am with a large organization; do you support other methods of installation besides the one I experienced from my trial?

We have additional methods of delivering product to the users in your organization. Please contact our sales or support team for details.

Do you have pricing for academia and non-profits?

Yes, we have aggressive pricing for students, educators and employees of certified nonprofit organizations. Contact our sales team for pricing details.

TABLE OF FIGURES SUPPORT

Figure 1: Gantt Chart	4
Figure 2: Assign Resources tab	5
Figure 3: List of Resource Types	5
Figure 4: Resource Sheet	6
Figure 5: Resource Usage View	6
Figure 6: Calendar	7
Figure 7: Hypernote panel	8
Figure 8: Milestone on the Gantt chart	8
Figure 9: Multiproject View	9
Figure 10: Project Report in spreadsheet (MS Excel®) format	10
Figure 11: Project Slide Preview	11
Figure 12: Project Dashboard	12
Figure 13: Project Mind Map	13

KEYBOARD SHORTCUTS

Following is an abbreviated list of the most commonly used keyboard shortcuts. See the in-program Help file for the comprehensive list.

Keystroke	Operation
Ctrl + N	Create a New Document
Ctrl + O	Open a Document
Ctrl + S	Save the active document
Ctrl + Shift + S	Save the active document under a new file name
Ctrl + P	Print Preview
Ctrl + F4	Close active document
Ctrl + Right	Indent task
Ctrl + Left	Outdent task
Ctrl + Down	Move item to the next position (one line down)
Ctrl + Up	Move item to the previous position (one line up)
Ctrl + L	Link selected tasks
Ctrl + Shift + L	Unlink selected tasks
Ctrl + Alt + G	Gantt Chart View
Ctrl + Alt + R	Resource List View
Ctrl + Alt + J	Projects Dashboard
Ctrl + Alt + U	Move to Resource Usage View
Ctrl + R	Call Reports dialog
Ctrl + Z	Undo the last operation
Ctrl + X	Cut the selection to the Document
Ctrl + C	Copy the selection to the Document
Ctrl + V	Paste the content from the Document
Ctrl + A	Select all the tasks on document
Esc	Deselect

CS Odessa

Contact Us

Technical Support/Sales

+18779001618 / +14244071041 Toll Free

https://helpdesk.conceptdraw.com/ticket.php

support@conceptdraw.com

© 2025, CS Odessa corp.
